you are not bound to accept the lowest or any Tender you receive.

The advance payment required is Rs.....

We undertake that, in competing for (and, if the award is made to us, in executing) the above contract, we will strictly observe the laws against fraud and corruption in force in India namely "Prevention of Corruption Act 1988".

We hereby confirm that this Tender complies with the Tender validity and Earnest money deposit required by the Tender documents.

We attach herewith our current income-tax clearance certificate.

Yours faithfully,

Authorized Signature:

Name & Title of Signatory: _____

Name of Tenderer _____

Address: _____

_____

Letter of Acceptance

(letterhead paper of the Employer)

.....[date]

To:

.....

.....[name and address of the Contractor]

Dear Sirs,

This is to notify you that your Tender dated ..... for execution of the .....

..... *[name of the contract and identification number, as given in the Instructions to Tenderers]* for the Contract Price of Rupees .....

..... (.....) [amount in words and figures], as corrected and modified in accordance with the Instructions to Tenderers is hereby accepted by our Agency.

You are hereby requested to furnish Security deposit plus additional security for unbalanced tenders in terms of Clause 25.5 of ITT, in the form detailed in Clause 29.1 of ITT for an amount of Rs..... within 20 days of the receipt of this letter of acceptance valid up to 30 days from the date of expiry of Defects Liability Period i.e. up to ..... and sign the contract, failing which action as stated in Para 29.4 of ITT will be taken.

Yours faithfully,

Authorized Signature

Name and Title of Signatory

Name of Agency

Issue of Notice to proceed with the work

(letterhead of the Employer)

.....(date)

To

.....

.....

..... (name and address of the Contractor)

Dear Sirs:

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

Pursuant to your furnishing the requisite security [illegible]
agreement for the construction of .....
Rs. ....., you are hereby instructed to proceed with the execution of the [illegible]
contract documents.

Yours faithfully,

(Signature, name and title of signatory
authorized to sign on behalf of Employer)

Agreement Form

Agreement

This agreement, made the .....day of .....20.....
between.....[name and address of Employer]
(hereinafter called "the Employer") of the one part and .....[name and
address of contractor] (hereinafter called "the Contractor") of the other part.

Whereas the Employer is desirous that the Contractor execute .....
.....[name and identification number of Contract] (hereinafter called "the Works") and the Employer has accepted the Tender by the Contractor for the execution and completion of such Works and the remedying of any defects therein at a contract price of Rupees.....

NOW THIS AGREEMENT WITNESSETH as follows:

1. In this Agreement, words and expression shall have the same meanings as are respectively assigned to them in the Conditions of Contract hereinafter referred to, and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy any defects therein in conformity in all aspects with the provisions of the Contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying the defects wherein the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.
4. The following documents shall be deemed to form and be read and construed as part of this Agreement, viz:
   i) Letter of Acceptance;
   ii) Notice to proceed with the works;
   iii) Contractor's Tender;
   iv) Contract Data;
   v) Conditions of contract (including Special Conditions of Contract);
   vi) Specifications;
   vii) Drawings;
   viii) Bill of Quantities; and
   ix) Any other document listed in the Contract Data as forming part of the contract.

In witness whereof the parties thereto have caused this Agreement to be executed the day and year first before written.

The Common Seal of .....
.....
was hereunto affixed in the presence of:
Signed, Sealed and Delivered by the said
.....
.....

in the presence of:
Binding Signature of Employer
.....

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

SECTION 5: CONDITIONS OF CONTRACT

Table of Contents

		Page No.
A.	**General**	
1.	Definitions	24
2.	Interpretation	24
3.	Law governing contract	25
4.	Employers decisions	25
5.	Delegation	25
6.	Communications	25
7.	Subcontracting	25
8.	Other Contractors	25
9.	Personnel	25
10.	Employer's and Contractor's risks	25
11.	Employer's risks	25
12	Contractor's risks	25
13.	Insurance	25
14.	Site Investigation Report	26
15	Query about Contract Data	26
16	Contractor to construct the Works	26
17.	The Works to be completed by Intended Completion Date	26
18	Approvals by the Employer	26
19.	Safety	27
20.	Discoveries	27
21.	Possession of the Site	27
22.	Access to the Site	27
23.	Instructions	27
24.	Procedure for resolution of disputes	27
B.	**Time Control**	
25.	Program	27
26.	Extension of the Intended Completion Date	28
27.	Delays ordered by the Employer	28
28.	Management meetings	28
C.	**Quality Control**	
29.	Identifying defects	28
30.	Tests	28
31.	Correction of defects	28
32.	Uncorrected defects	28
D.	**Cost Control**	
33	Bill of Quantities (BOQ)	29
34	Variations	29
35.	Payment for Variations	29
36.	Submission of bills for payment	29
37	Payments	30
38.	Compensation events	30
39.	Tax	30
40	Price Adjustment	30
41.	Liquidated damages	31
42.	Advance Payments	31
43.	Securities	31
44.	Cost of repairs	32
E	**Finishing of Contract**	
45.	Completion	32
46.	Taking Over	32
47.	Final account	32
48.	As built drawings and/or Operating and Maintenance Manuals	32
49.	Termination	32
50	Payment upon termination	33
51.	Property	33
52.	Release from performance	33
F	**Special Conditions of Contract**	34

Manjunath.S.R

Executive Engineer
Project Director
Yelahanka
BBMP, Bangalore-92

Scanned by TapScanner

1. **Definitions**

1.1 Terms which are defined in the Contract Data are not also defined in the Conditions of Contract but keep their defined meanings. Bold letters are used to identify defined terms.

Bill of Quantities means the priced and completed Bill of Quantities forming part of the Tender.
Compensation events are those defined in Clause 38 hereunder.
The **Completion Date** is the date of completion of the Works as certified by the Employer in accordance with Sub Clause 46.1.
The **Contract** is the contract between the Employer and the Contractor to execute, complete and maintain the Works. It consists of the documents listed in Clause 2.2 below.
The **Contract Data** defines the documents and other information which comprise the Contract.
The **Contractor** is a person or corporate body whose Tender to carry out the Works has been accepted by the Employer.
The **Contractor's Tender** is the completed Tender document submitted by the Contractor to the Employer.
The **Contract price** is the price stated in the Letter of Acceptance and thereafter as adjusted in accordance with the provisions of the Contract.
Days are calendar days; **months** are calendar months.
A **Defect** is any part of the Works not completed in accordance with the Contract.
The **Defects liability period** is the period named in the Contract Data and calculated from the Completion Date.
The **Employer** is the party who will employ the Contractor to carry out the Works.
Equipment is the Contractor's machinery and vehicles brought temporarily to the Site to construct the Works.
The **Initial Contract price** is the Contract Price listed in the Employer's Letter of Acceptance.
The **Intended Completion Date** is the date on which it is intended that the Contractor shall complete the Works. The Intended Completion Date is specified in the Contract Data. The Intended Completion Date may be revised only by the Employer by issuing an extension of time.
Materials are all supplies, including consumables, used by the contractor for incorporation in the Works.
Plant is any integral part of the Works which is to have a mechanical, electrical, electronic or chemical or biological function.
The **Site** is the area defined as such in the Contract Data.
Specification means the Specification of the Works included in the Contract and any modification or addition made or approved by the Employer.
The **Start Date** is given in the Contract Data. It is the date when the Contractor shall commence execution of the works. It does not necessarily coincide with any of the Site Possession Dates.
A **Subcontractor** is a person or corporate body who has a Contract with the Contractor to carry out a part of the work in the Contract which includes work on the Site.
A **Variation** is an instruction given by the Employer which varies the Works.
The **Works** are what the Contract requires the Contractor to construct, install, and turn over to the Employer, as defined in the Contract Data.

2. **Interpretation**

2.1 In interpreting these Conditions of Contract, singular also means plural, male also means female or neuter, and the other way around. Headings have no significance. Words have their normal meaning under the language of the Contract unless specifically defined. The Employer will provide instructions clarifying queries about the Conditions of Contract.

2.2 The documents forming the Contract shall be interpreted in the following order of priority:

(1) Agreement
(2) Letter of Acceptance, notice to proceed with the works
(3) Contractor's Tender
(4) Contract Data
(5) Conditions of Contract
(6) Specifications
(7) Drawings
(8) Bill of quantities and
(9) any other document listed in the Contract Data as forming part of the Contract.

3. **Law governing contract**

3.1 The law governing the Contract is the Laws of India supplanted by the Karnataka Local Acts.

4. **Employer's decisions**

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

Employer and the Contractor.

6. **Delegation**

6.1 The Employer may delegate any of his duties and responsibilities to other people after notifying the Contractor and may cancel any delegation after notifying the Contractor.

7. **Communications**

7.1 Communications between parties which are referred to in the conditions are effective only when in writing. A notice shall be effective only when it is delivered (in terms of Indian Contract Act).

7. **Subcontracting**

7.1 The Contractor may subcontract with the approval of the Employer but may not assign the Contract without the approval of the Employer in writing. Subcontracting does not alter the Contractor's obligations.

8. **Other Contractors**

8.1 The Contractor shall cooperate and share the Site with other contractors, public authorities, utilities, and the Employer.

9. **Personnel**

9.1 The Contractor shall employ the technical personnel (of number and qualifications) as may be stipulated by GOK from time to time during the execution of the work. The technical staff so employed shall be available at site as may be stipulated by the Employer.

9.2 If the Employer asks the Contractor to remove a person who is a member of the Contractor's staff or his work force stating the reasons, the Contractor shall ensure that the person leaves the Site within seven days and has no further connection with the work in the Contract.

9.3 The Contractor shall provide one four wheeler along with driver, fuel expenses to Project Engineers in-charge of work to facilitate and co-ordinate the supervision of the work as the work is clustered in different areas.

10. **Employer's and Contractor's risks**

10.1 The Employer carries the risks which this Contract states are Employer's risks, and the Contractor carries the risks which this Contract states are Contractor's risks.

11. **Employer's risks**

11.1 The Employer is responsible for the excepted risks which are:

(a) rebellion, riot commotion or disorder unless solely restricted to employees of the Contractor or his Sub-Contractors arising from the conduct of the Works; or

(b) a cause due solely to the design of the Works, other than the Contractor's design; or

(c) any operation of the forces of nature (in so far as it occurs on the Site) which an experienced contractor:

(i) could not have reasonably foreseen; or

(ii) could reasonably have foreseen, but against which he could not reasonably have taken at least one of the following measures;

(A) prevent loss or damage to physical property from occurring by taking appropriate measures or

(B) insure against such loss or damage

12. **Contractor's risks**

12.1 All risks of loss of or damage to physical property and of personal injury and death which arise during and in consequence of the performance of the Contract other than the excepted risks are the responsibility of the Contractor.

13. **Insurance:**

13.1 The Contractor shall prior to commencing the works, effect and thereafter maintain insurances , in the joint names of the Employer and the Contractor, (cover from the first working day after the Start Date to the end of Defects Liability Period), in the amounts stated in the Contract Data :

(a) for loss of or damage to the Works, Plants and Materials and the Contractor's equipment;

anjuth L.S.R

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

(b) for liability of both Parties for loss, damage, [illegible] of the Contractor's performance of the Contract including the [illegible] damage Employer's property other than the Works and

(c) for liability of both Parties and of any Employer's representative for death and injury to the Contractor's personnel except to the extent that liability arises from the negligence of the Employer, any Employer's representative or their Employees.

13.2 Policies and certificates for insurance shall be delivered by the Contractor to the Employer for his approval before the Start Date. All such insurance shall provide for compensation to be payable to rectify the loss or damage incurred. All payments received from insurers relating to loss or damage shall be held jointly by the Parties and used for the repair of the loss or damage or as compensation for loss or damage that is not to be repaired.

13.3 If the Contractor fails to effect or keep in force any of the insurances referred to in the previous sub-clauses or fails to provide satisfactory evidence, policies or receipts, the Employer may without prejudice to any other right or remedy, effect insurance for the cover relevant to such default and pay the premiums due and recover the same as a deduction from any other monies due to the Contractor. If no payments is due, the payment of the premiums shall be a debt due.

13.4 Alterations to the terms of an insurance shall not be made without the approval of the Employer.

13.5 Both Parties shall comply with any conditions of the insurance policies.

14. Site Investigation Reports:

14.1 The Contractor, in preparing the tender, shall rely on any site investigation reports referred to in the Contract data, supplemented by any information available to the Tenderer.

15. Queries about the Contract Data

15.1 The Employer will clarify queries on the Contract Data.

16. Contractor to construct the Works

16.1 The Contractor shall construct the Works in accordance with the Specification and Drawings.

17. The Works to be completed by the Intended Completion Date

17.1 The Contractor may commence execution of the Works on the Start Date and shall carry out the Works in accordance with the program submitted by the Contractor, as updated with the approval of the Employer, and complete them by the Intended Completion Date.

18. Approval by the Employer:

18.1 The Contractor shall submit Specification and drawings showing the proposed Temporary Works to the Employer, who is to approve them if they comply with the Specifications and Drawings.

18.2 The Contractor shall be responsible for the design of Temporary Works

18.3 The Employer's approval shall not alter the Contractor's responsibility for design of the Temporary Works.

18.4 The Contractor shall obtain approval of third parties to the design of third parties to the design of the temporary Works where required.

18.5 All Drawings prepared by the Contractor for the execution of the temporary or permanent Works, are subject to prior approval by the Employer before their use.

19. Safety

19.1 The Contractor shall be responsible for the safety of all activities on the Site.

20. Discoveries

20.1 Anything of historical or other interest or of significant value unexpectedly discovered on the Site is the property of the Employer. The Contractor is to notify the Employer of such discoveries and carry out the Employer's instructions for dealing with them.

21. Possession of the Site

21.1 The Employer shall give possession of all parts of the Site to the Contractor. If possession of a part is not given by the date stated in the Contract Data the Employer is deemed to have delayed the start of the relevant activities and this will be Compensation Event.

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

shall allow the Employer and any person authorized by the Employer access to the Site, to any place where work in connection with the Contract is being carried out or is intended to be carried out and to any place where materials or plant are being manufactured / fabricated / assembled for the works.

23. **Instructions**

23.1 The Contractor shall carry out all instructions of the Employer which comply with the applicable laws where the Site is located.

24. **Procedure for resolution of Disputes:**

24.1 If the Contractor is not satisfied with the decision taken by the Employer, the dispute shall be referred by either party to Arbitration within 30 days of the notification of the Employer's decision.

24.2 If neither party refers the dispute to Arbitration within the above 30 days, the Employer's decision will be final and binding.

24.3 The Arbitration shall be conducted in accordance with the arbitration procedure stated in the Special Conditions of Contract.

B. Time Control

25. **Program**

25.1 Within the time stated in the Contract Data the Contractor shall submit to the Employer for approval a Program showing the general methods, arrangements, order, and timing for all the activities in the Works.

25.2 The Employer's approval of the Program shall not alter the Contractor's obligations. The Contractor may revise the Program and submit it to the Employer again at any time. A revised Program is to show the effect of Variations and Compensation Events.

26. **Extension of the Intended Completion Date**

26.1 The Employer shall extend the Intended Completion Date if a Compensation Event occurs or a Variation is issued which makes it impossible for Completion to be achieved by the Intended Completion Date.

26.2 The Employer shall decide whether and by how much to extend the Intended Completion Date within 21 days of the Contractor asking the Employer for a decision upon the effect of a Compensation Event or Variation and submitting full supporting information.

27. **Delays ordered by the Employer**

27.1 The Employer may instruct the Contractor to delay the start or progress of any activity within the Works.

28. **Management meetings**

28.1 The Employer may require the Contractor to attend a management meeting. The business of a management meeting shall be to review the progress achieved and the plans for remaining work.

28.2 The responsibility of the parties for actions to be taken is to be decided by the Employer either at the management meeting or after the management meeting and stated in writing to be distributed to all who attended the meeting.

C. Quality Control

29. **Identifying defects**

29.1 The Employer shall check the Contractor's work and notify the Contractor of any Defects that are found. Such checking shall not affect the Contractor's responsibilities. The Employer may instruct the Contractor to search for a Defect and to uncover and test any work that the Employer considers may have a Defect

30. **Tests**

30.1 If the Employer instructs the Contractor to carry out a test not specified in the Specification to check whether any work has a Defect and the test shows that it does, the Contractor shall pay for the test and any samples. If there is no Defect the test shall be a Compensation Event.

Manjunath.S.R

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

Page 26 of 34

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

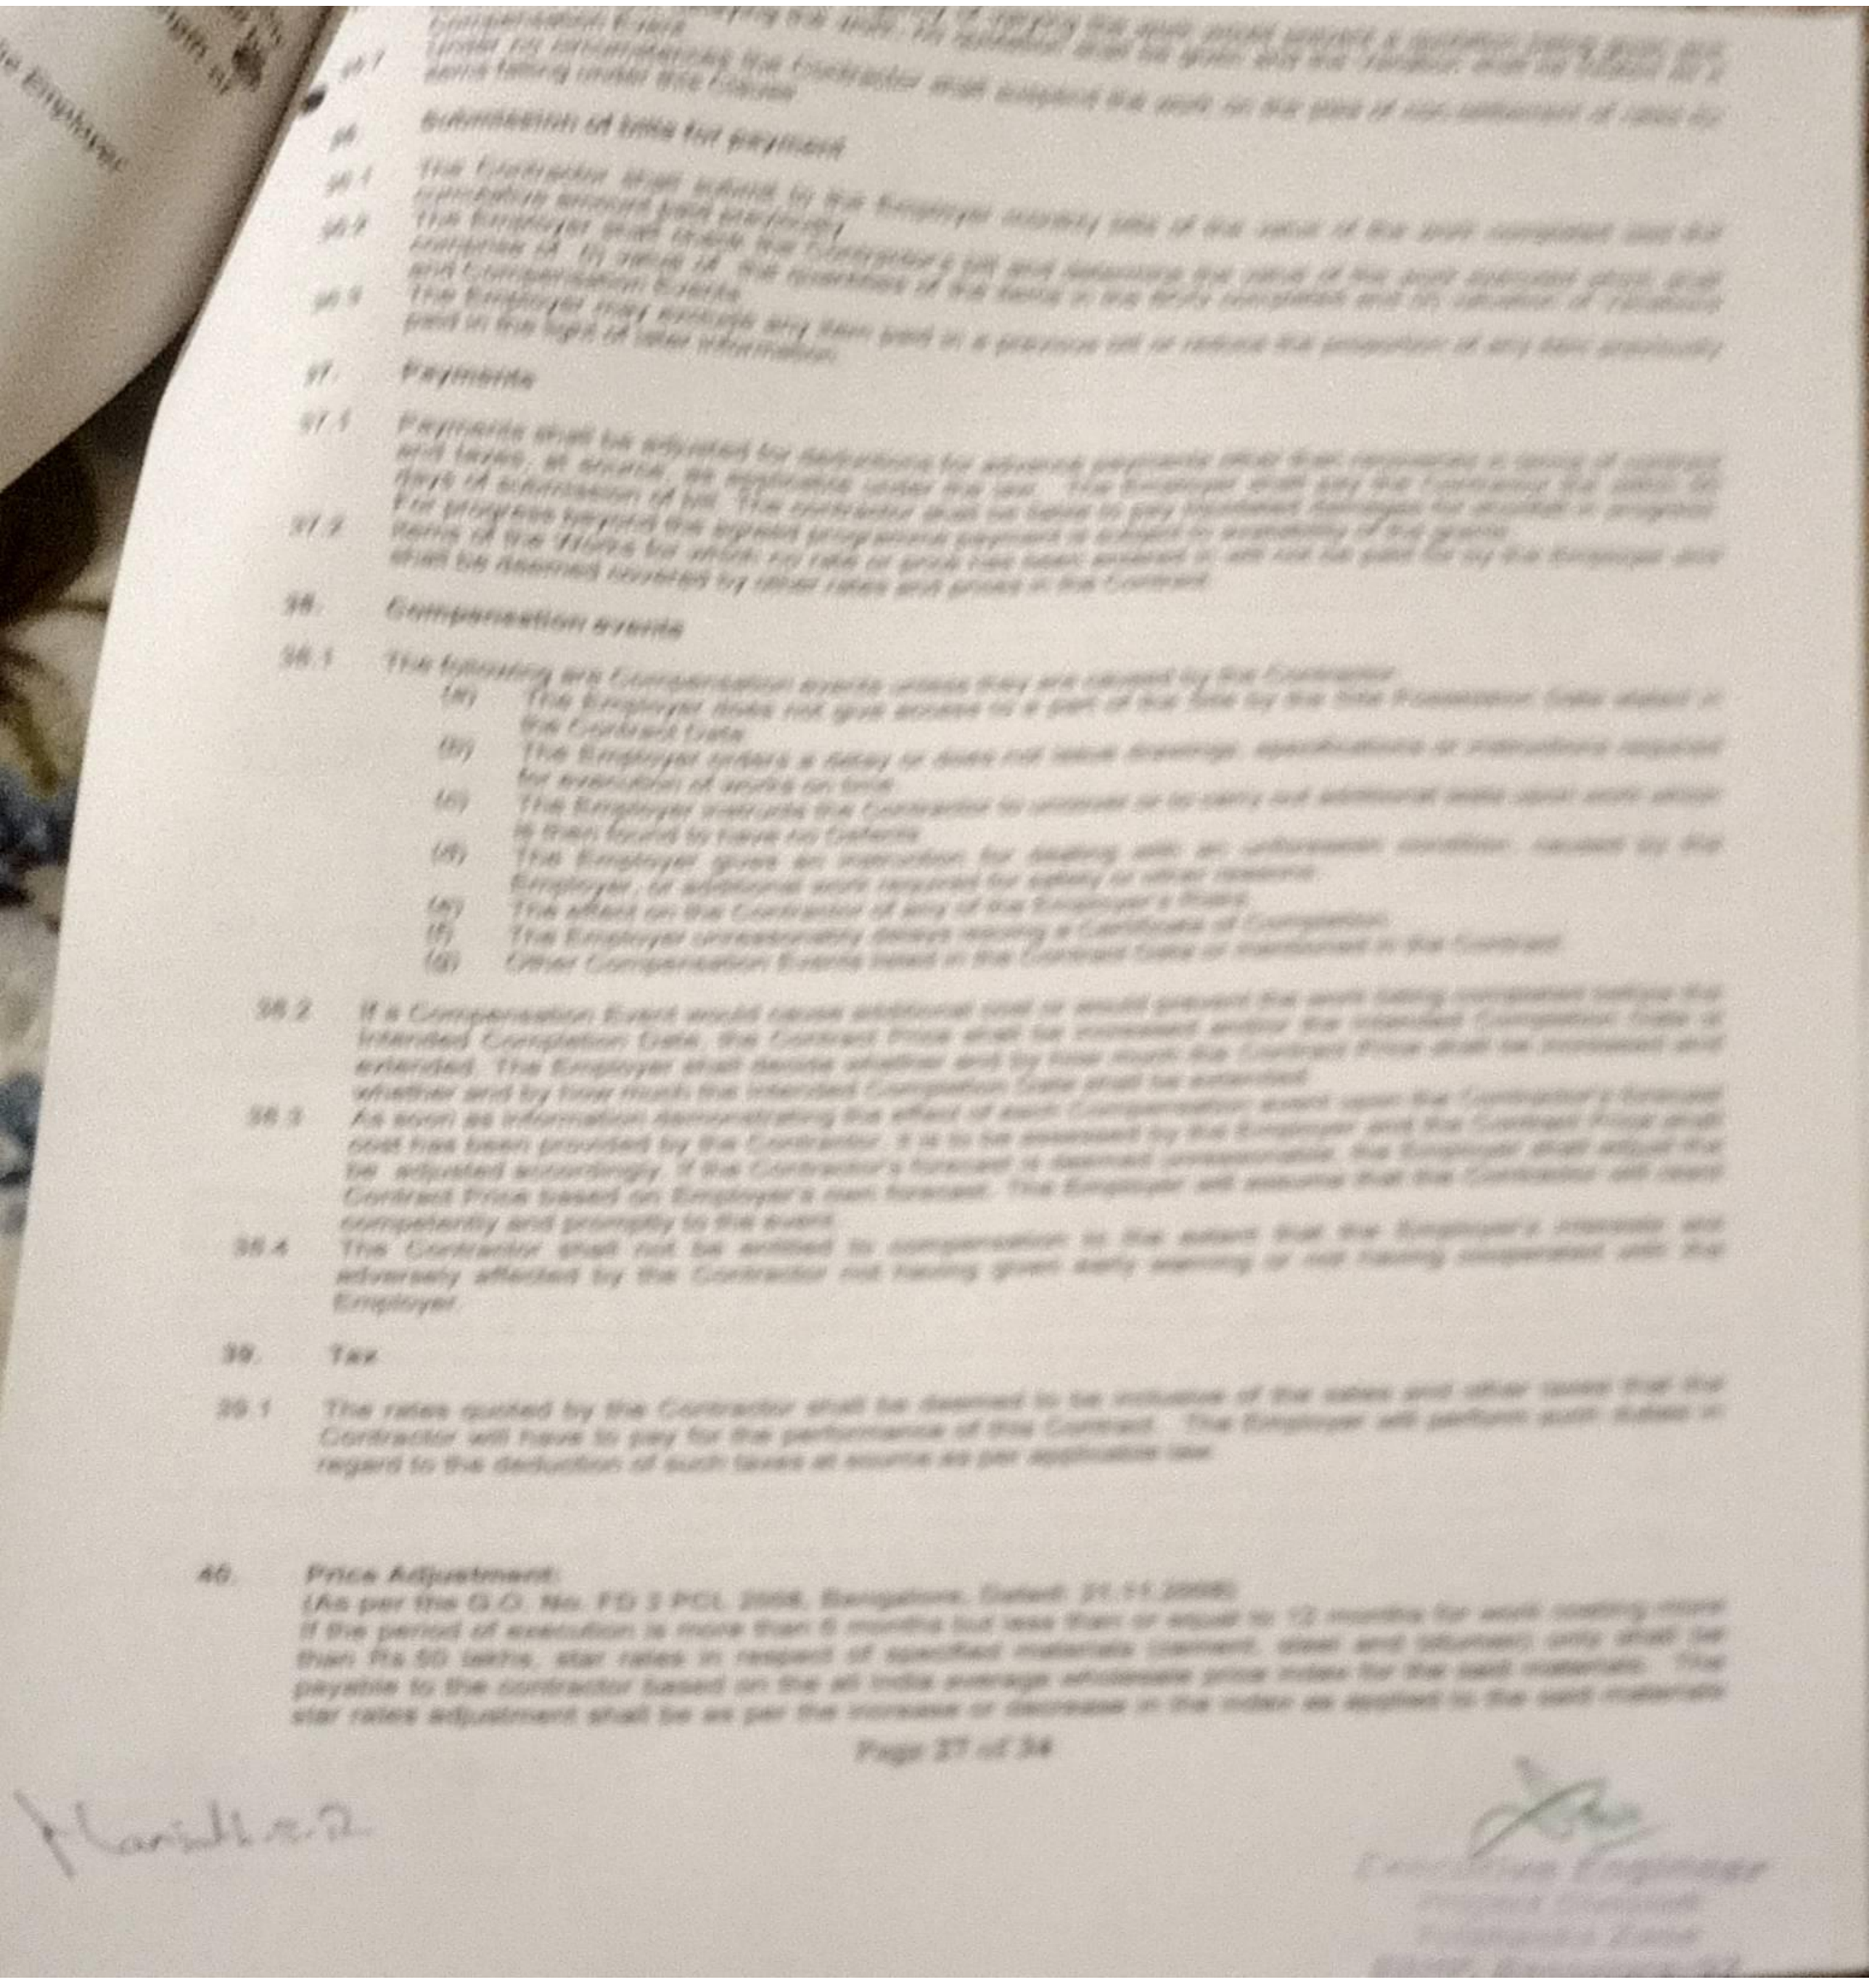

Scanned by TapScanner

between the last date for receiving bids and the [illegible] submitted by the contractor at the time of execution of agreement which shall mandatorily be a part of the agreement.

40.1 Deleted

40.2 Deleted

41. Liquidated damages

41.1 The Contractor shall pay liquidated damages to the Employer at the rate per day stated in the Contract Data for each day that the Completion Date is later than the Intended Completion Date (for the whole of the works or the milestone as stated in the Contract Data). The total amount of liquidated damages shall not exceed the amount defined in the Contract Data. The Employer may deduct liquidated damages from payments due to the Contractor. Payment of liquidated damages does not affect the Contractor's liabilities.

41.2 If the Intended Completion Date is extended after liquidated damages have been paid, the Employer shall correct any overpayment of liquidated damages by the Contractor by adjusting the next payment of bill.

42. Advance Payments: (DELETED)

43. Securities:

43.1 The Security deposit (including additional security for unbalanced tenders) shall be provided to the Employer no later than the date specified in the Letter of Acceptance and shall be issued in an amount and form and type of instrument acceptable to the Employer. The Security deposit shall be valid until a date 30 days from the date of expiry of Defects Liability Period and the additional security for unbalanced tenders shall be valid until a date 30 days from the date of issue of the certificate of completion.

44. Cost of Repairs:

44.1 Loss or damage to the Works or Materials to be incorporated in the Works between the Start Date and the end of the Defects Correction periods shall be remedied by the Contractor at the Contractor's cost if the loss or damage arises from the Contractor's acts or omissions.

45. Completion **E. Finishing the Contract**

45.1 The Contractor shall request the Employer to issue a Certificate of Completion of the Works and the Employer will do so upon deciding that the Work is completed.

46. Taking over

46.1 The Employer shall take over the Site and the Works within seven days of issuing a certificate of Completion.

47. Final account

47.1 The Contractor shall supply to the Employer a detailed account of the total amount that the Contractor considers payable under the Contract before the end of the Defects Liability Period. The Employer shall issue a Defect Liability Certificate and certify any final payment that is due to the Contractor within 90 days of receiving the Contractor's account if it is correct and complete. If it is not, the Employer shall issue within 90 days a schedule that states the scope of the corrections or additions that are necessary. If the Final Account is still unsatisfactory after it has been resubmitted, the Employer shall decide on the amount payable to the Contractor and make payment within 60 days of receiving the Contractor's revised account.

48. As built drawings and /or Operating and Maintenance Manuals

48.1 If "as built"(*Completion drawings*) Drawings and/or operating and maintenance manuals are required, the Contractor shall supply them by the dates stated in the Contract Data.

48.2 If the Contractor does not supply the Drawings by the dates stated in the Contract Data, or they do not receive the Employer's approval, the Employer shall withhold the amount stated in the Contract Data from payments due to the Contractor.

49. Termination

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

(e) ... suspends for ten (10) ... [illegible] ... Contract;

(f) ... suspends for 28 days ... [illegible] ... Contract;

(g) ... becomes bankrupt or goes into liquidation other than for a reconstruction or amalgamation;

(h) ... fails to correct a particular defect is a fundamental breach of Contract and the Contractor fails to correct it within a reasonable period of time determined by the Employer;

(i) ... does not maintain a security which is required;

(j) ... has delayed the completion of works by the number of days for which the maximum amount of liquidated damages can be paid as defined in the Contract data; and

(k) ... in the judgment of the Employer has engaged in corrupt or fraudulent practices in competing for or in executing the Contract.

For the purposes of this paragraph: "corrupt practice" means the offering, giving, receiving or soliciting of anything of value to influence the action of a public official in the procurement process or in contract execution. "Fraudulent practice" means a misrepresentation of facts in order to influence a procurement process or the execution of a contract to the detriment of the Borrower, and includes collusive practice among Tenderers (prior to or after Tender submission) designed to establish Tender prices at artificial non-competitive levels and to deprive the Borrower of the benefits of free and open competition."

49.3 When either party to the Contract gives notice of a breach of contract to the Employer for a cause other than those listed under Sub Clause 49.2 above, the Employer shall decide whether the breach is fundamental or not.

49.4 Notwithstanding the above, the Employer may terminate the Contract for convenience.

49.5 If the Contract is terminated the Contractor shall stop work immediately, make the Site safe and secure and leave the Site as soon as reasonably possible.

50. Payment upon Termination

50.1 If the Contract is terminated because of a fundamental breach of Contract by the Contractor, the Employer shall prepare bill for the value of the work done less advance payments received up to the date of the bill, less other recoveries due in terms of the contract, less taxes due to be deducted at source as per applicable law and less the percentage to apply to the work not completed as indicated in the Contract Data. Additional Liquidated Damages shall not apply. If the total amount due to the Employer exceeds any payment due to the Contractor the difference shall be a debt payable to the Employer.

50.2 If the Contract is terminated at the Employer's convenience or because of a fundamental breach of Contract by the Employer, the Employer shall prepare bill for the value of the work done, the reasonable cost of removal of Equipment, repatriation of the Contractor's personnel employed solely on the Works, and the Contractor's costs of protecting and securing the Works and less advance payments received up to the date of the certificate, less other recoveries due in terms of the contract, and less taxes due to be deducted at source as per applicable law and make payment accordingly.

51. Property

51.1 All materials on the Site, Plant, Equipment, Temporary Works and Works are deemed to be the property of the Employer, if the Contract is terminated because of a Contractor's default.

52. Release from performance

52.1 If the Contract is frustrated by any event entirely outside the control of either the Employer or the Contractor the Employer shall certify that the Contract has been frustrated. The Contractor shall make the Site safe and stop work as quickly as possible after receiving this certificate and shall be paid for all work carried out before receiving it and for any work carried out afterwards to which commitment was made.

F. Special Conditions of Contract

1. Labour:

The Contractor shall, unless otherwise provided in the Contract, make his own arrangements for the engagement of all staff and labour, local or other, and for their payment, housing, feeding and transport.

The Contractor shall, if required by the Employer, deliver to the Employer a return in detail, in such form and at such intervals as the Employer may prescribe, showing the staff and the numbers of the several classes

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

(f) labour hour long to bore employed by the Contractor on the site and such other information as Employer may require.

3. **Compliance with labour regulations**

During continuance of the contract, the Contractor and his sub contractors shall abide at all times by all existing labour enactments and rules made there under, regulations, notifications and bye laws of the State or the Central Government or local authority and any other labour law (including rules), regulations, bye laws that may be passed or notification that may be issued under any labour law in future either by the State or the Central Government or the local authority. The Contractor shall keep the Employer indemnified in case any action is taken against the Employer by the competent authority on account of contravention of any of the provisions of any Act or rules made there under, regulations or notifications including amendments if the Employer is caused to pay or reimburse, such amounts as may be necessary to cause or observe, or for non-observance of the provisions stipulated in the notifications/bye laws/Acts/Rules/regulations including amendments, if any, on the part of the Contractor, Employer shall have the right to deduct any money due to the Contractor including his amount of security deposit. The Employer shall also have right to recover from the Contractor any sum required or estimated to be required for making good the loss or damage suffered by the Employer.

The employees of the Contractor and the Sub-Contractor in no case shall be treated as the employees of the Employer at any point of time.

3. **Protection of Environment:**

The contractor shall take all reasonable steps to protect the environment on and off the Site and to avoid damage or nuisance to persons or to property of the public or others resulting from pollution, noise or other causes arising as a consequence of his methods of operation. During continuance of the contract, the contractor and his sub-contractors shall abide at all times by all existing enactments on environmental protection and rules made there under, regulations, notifications and bye-laws of the State or Central Government, or local authorities and any other law, bye-law, regulations that may be passed or notification that may be issued in this respect in future by the State or Central Government or the local authority.

4. **Arbitration (Clause 24)**

4.1 Deleted

5. In the case of the death of a Contractor after executing the agreement / commencement of the work, his legal heir, if an eligible registered Contractor and willing can execute and complete the work at the accepted tender rates irrespective of the cost of the work.

6. The defect liability period is 3 years Security deposit amount will be released only after satisfactory completion of defect liability period.

[Add other Clauses specific to the work for which tenders are invited.]

Annexure;

LIST OF ORGANIZATIONS WHO ARE CONSIDERED AS APPOINTING AUTHORITY FOR APPOINTMENT OF ARBITRATORS[7]

1. Indian Council of Arbitration, New Delhi;
2. International Centre for Alternative Disputes Resolution (India);
3. Indian Roads Congress;
4. Indian Building Congress;
5. Indian Institute of Bridge Engineers;
6. Indian Institute of Public Health Engineers;
7. Institute of Water Works

[7] Add any other Organization considered suitable.

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

SECTION 6: CONTRACT DATA

Clauses marked "N/A" do not apply in this Contract.

The following documents are also part of the Contract:

- The Schedule of Operating and Maintenance Manuals — Clause Reference [45]
- The Methodology and Program of Construction — [25]
- Site Investigation Reports — [14]
- The Schedule of Key and Critical Equipment to be deployed on the work as per agreed program of construction. — [25]

The Employer is: — [1.1]
Name: The Commissioner
Address: BBMP, N.R. Square Bangalore-02

Name of authorized Representative Executive Engineer
Project Division – Yelahanka Zone
Bruhat Bangalore Mahanagara Palike

The name and identification number of the Contract is

Works for **Improvements to roads, drains and construction of culverts at Central Excise layout, hegdenagara and Surrounding areas in Ward No.06**

The start date shall be the date of issue of notice to proceed with the work. [1.1]

The Intended Completion Date for the whole of the Works is 06 Months with the following milestones

Milestone dates:

The Site Possession Date is: Date of work order [21]

The Site is located at **Yelahanka Zone** , [1.1]
and is defined in drawings nos.

The Defects Liability Period is 2 Years. [31]

Insurance requirements are as under: [13]

	Type of Cover	Minimum cover for Insurance
(i)	Works and of Plant and materials	The sum stated in the Agreement plus 20%
(ii)	Loss or damage to equipment	Full replacement cost
(iii)	Loss or damage to property of Third Party	Full replacement cost
(iv)	Personal injury or death insurance (a) for Third Party	
	(b) for Contractor's employees or labour	In accordance with the statutory requirements applicable to Karnataka

Price Adjustment Formula; **(DELETED)** [40]

Executive Engineer
Project Division

Scanned by TapScanner

The maximum amount of liquidated damages for the whole of the works is Ten percent of final contract price. [41]

Repayment of advance payment for mobilization: **(DELETED)** [42]

The date by which "as-built" drawings (in scale 1 in 1000) in 2 sets are required is within 30 days of issue of certificate of completion of Whole or Section of the Work as the case may be. [48]

The date by which Operating and Maintenance Manuals are required is within 30 days of issue of certificate of completion of Whole or Section of the Work as the case may be. [48]

The amount to be withheld for failing to supply "as built" drawings or supply of Operation and Maintenance Manuals by the date required is [48]

The following events shall also be fundamental breach of the contract: [49.2]

1. The contractor has contravened Sub-clause 7.1 and Clause 9 of CC.

The percentage to apply to the value of the work not completed representing the Employer's [60.1]

Additional cost for completing the Works shall be 30 percent (30%).
The tenderer must have 50% of the The following materials and remaining 50 % of the materials procured on lease/ Hire basis

Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore-92

Scanned by TapScanner

SECTION 8: DRAWINGS
(Enclosed)

SECTION 10: FORMAT OF BANK GUARANTEE FOR SECURITY DEPOSIT

To ..... *[name of Employer]*
..... *[address of Employer]*

WHEREAS ..... *[name and address of Contractor]* (hereinafter called "the Contractor") has undertaken, in pursuance of Contract No. ..... dated : ..... to execute .....*[name of Contract and brief description of Works]* (hereinafter called "the Contract");

AND WHEREAS it has been stipulated by you in the said Contract that the Contractor shall furnish you with a Bank Guarantee by a recognized bank for the sum specified therein as security for compliance with his obligations in accordance with the Contract;

AND WHEREAS we have agreed to give the Contractor such a Bank Guarantee;

NOW THEREFORE we hereby affirm that we are the Guarantor and responsible to you, on behalf of the Contractor, up to a total of Rs. ..... *[amount of guarantee]*[8]_Rupees.....*[in words]*, and we undertake to pay you, upon your first written demand and without cavil or argument, any sum or sums within the limits of ..... *[amount of guarantee]*[9] as aforesaid without your needing to prove or to show grounds or reasons for your demand for the sum specified therein.

We hereby waive the necessity of your demanding the said debt from the Contractor before presenting us with the demand.

We further agree that no change or addition to or other modification of the terms of the Contract or of the Works to be performed there under or of any of the Contract documents which may be made between you and the Contractor shall in any way release us from any liability under this guarantee, and we hereby waive notice of any such change, addition or modification.

This guarantee shall be valid until 30 days from the date of expiry of the Defects Liability Period.

Signature and seal of the guarantor _____
Name of Bank _____
Address _____
Date _____

[8] An amount shall be inserted by the Guarantor, representing the percentage of the Contract Price specified in the Contract

Scanned by TapScanner
